


Project Schedule




Oswegatchie Fire Station

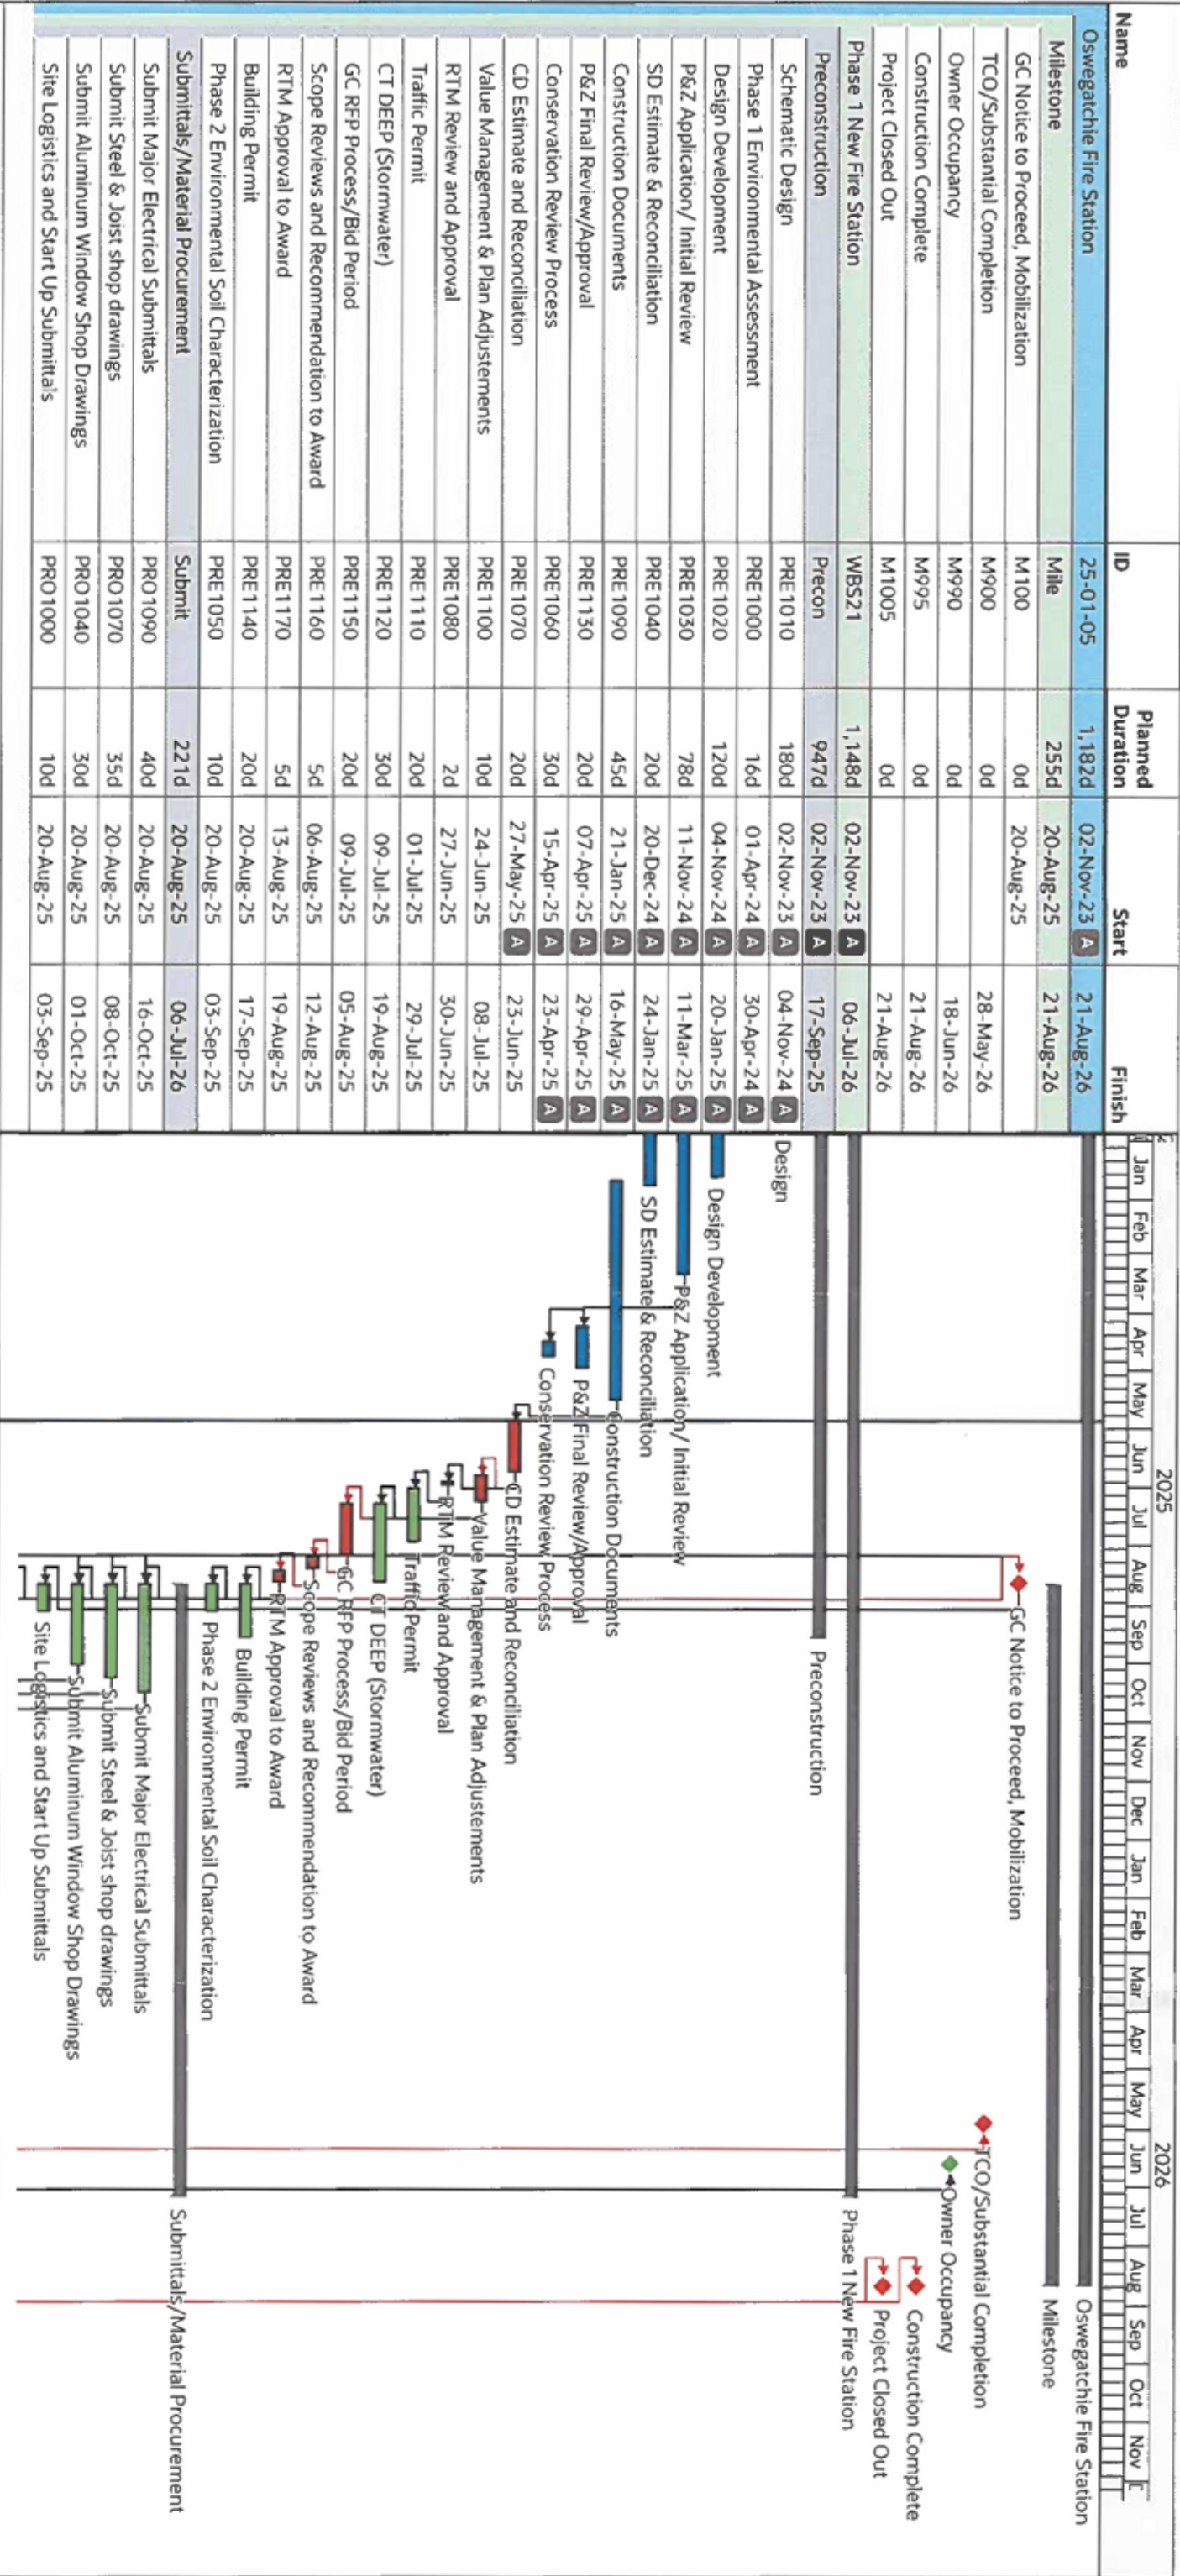

Date	Revision	Checked	Approved
04-Mar-25	Update		
20-May-25	Update		
27-May-25	Update		

Waterford Connecticut

Project Schedule

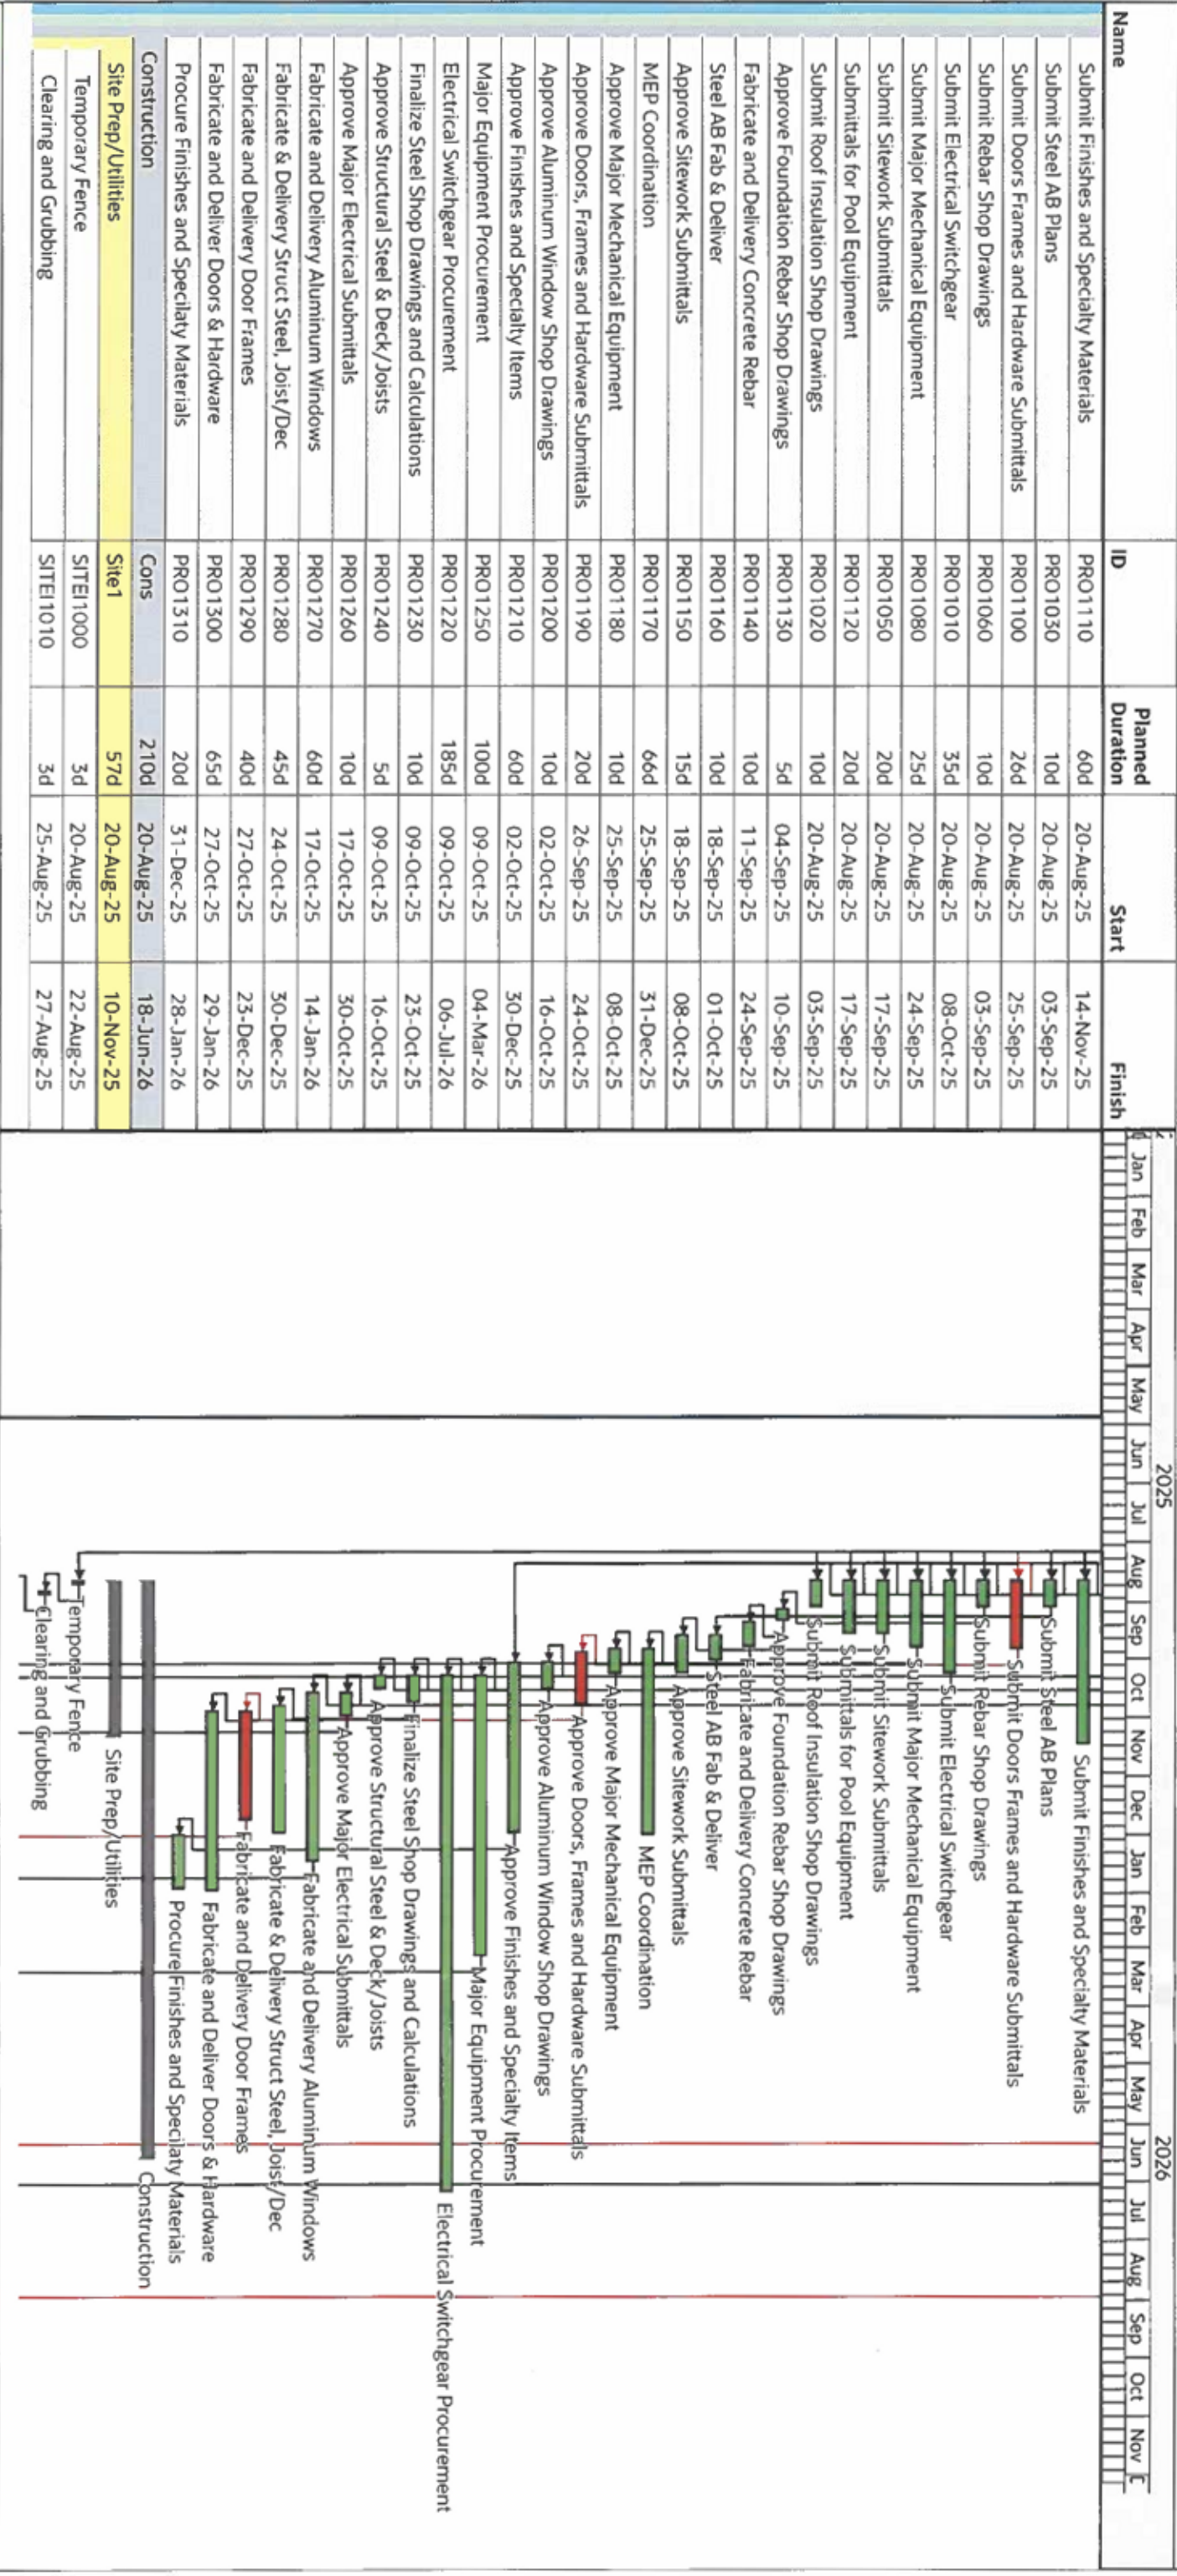

Oswegatchie Fire Station




DOWNES

Waterford Connecticut

Date	Revision	Checked	Approved
04-Mar-25	Update		
20-May-25	Update		
27-May-25	Update		

Project Schedule

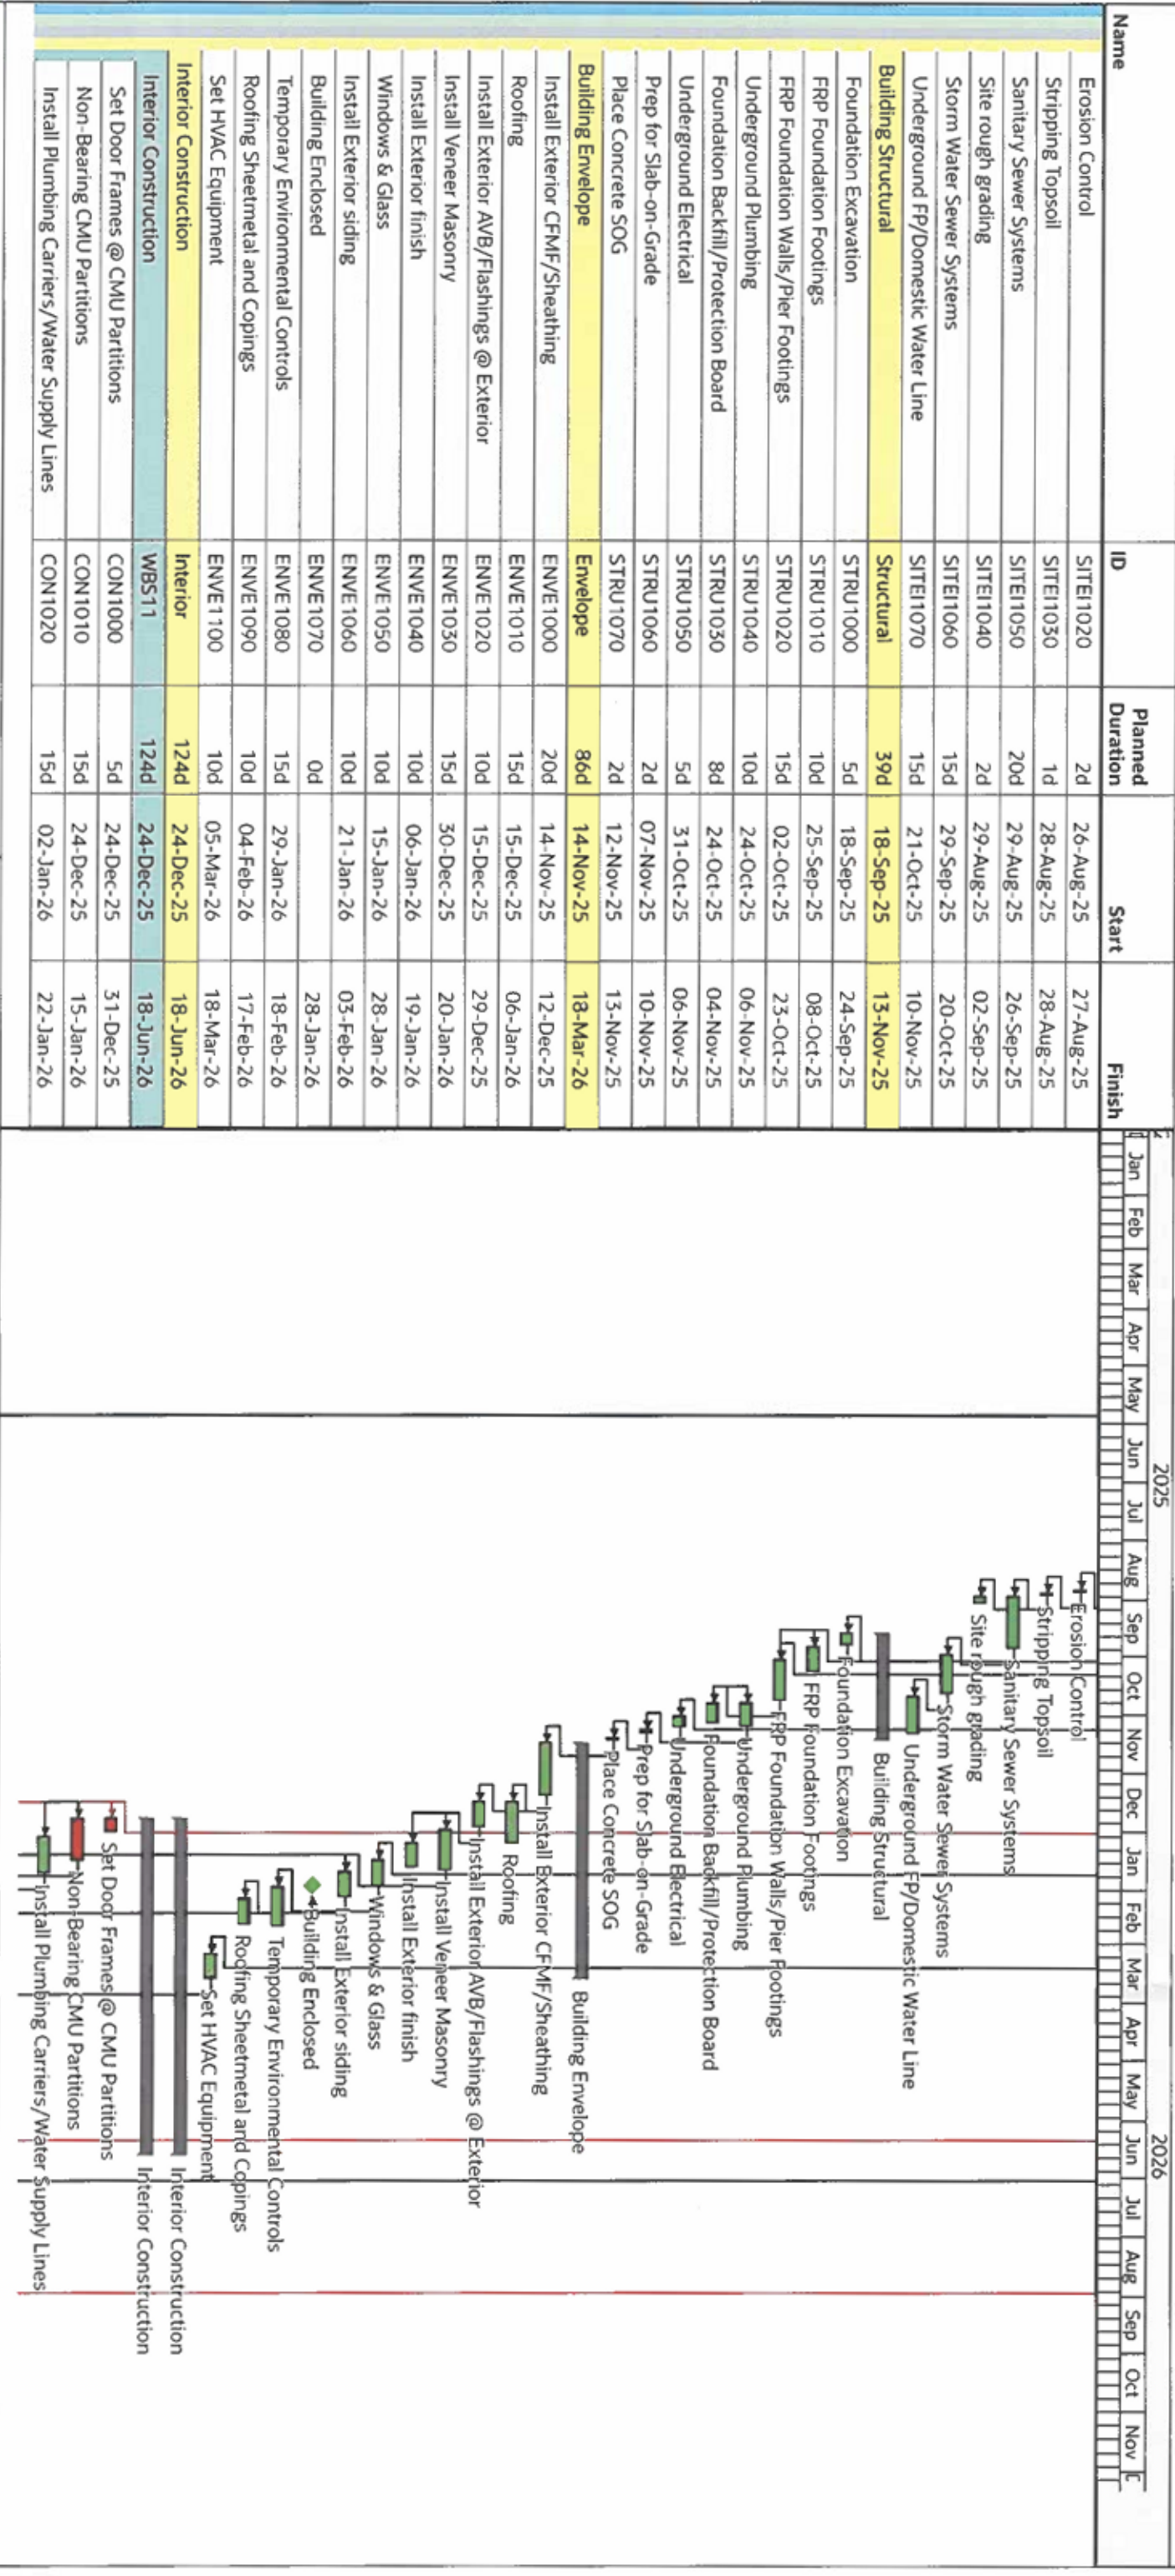


Oswegatchie Fire Station

Waterford Connecticut



Project Schedule

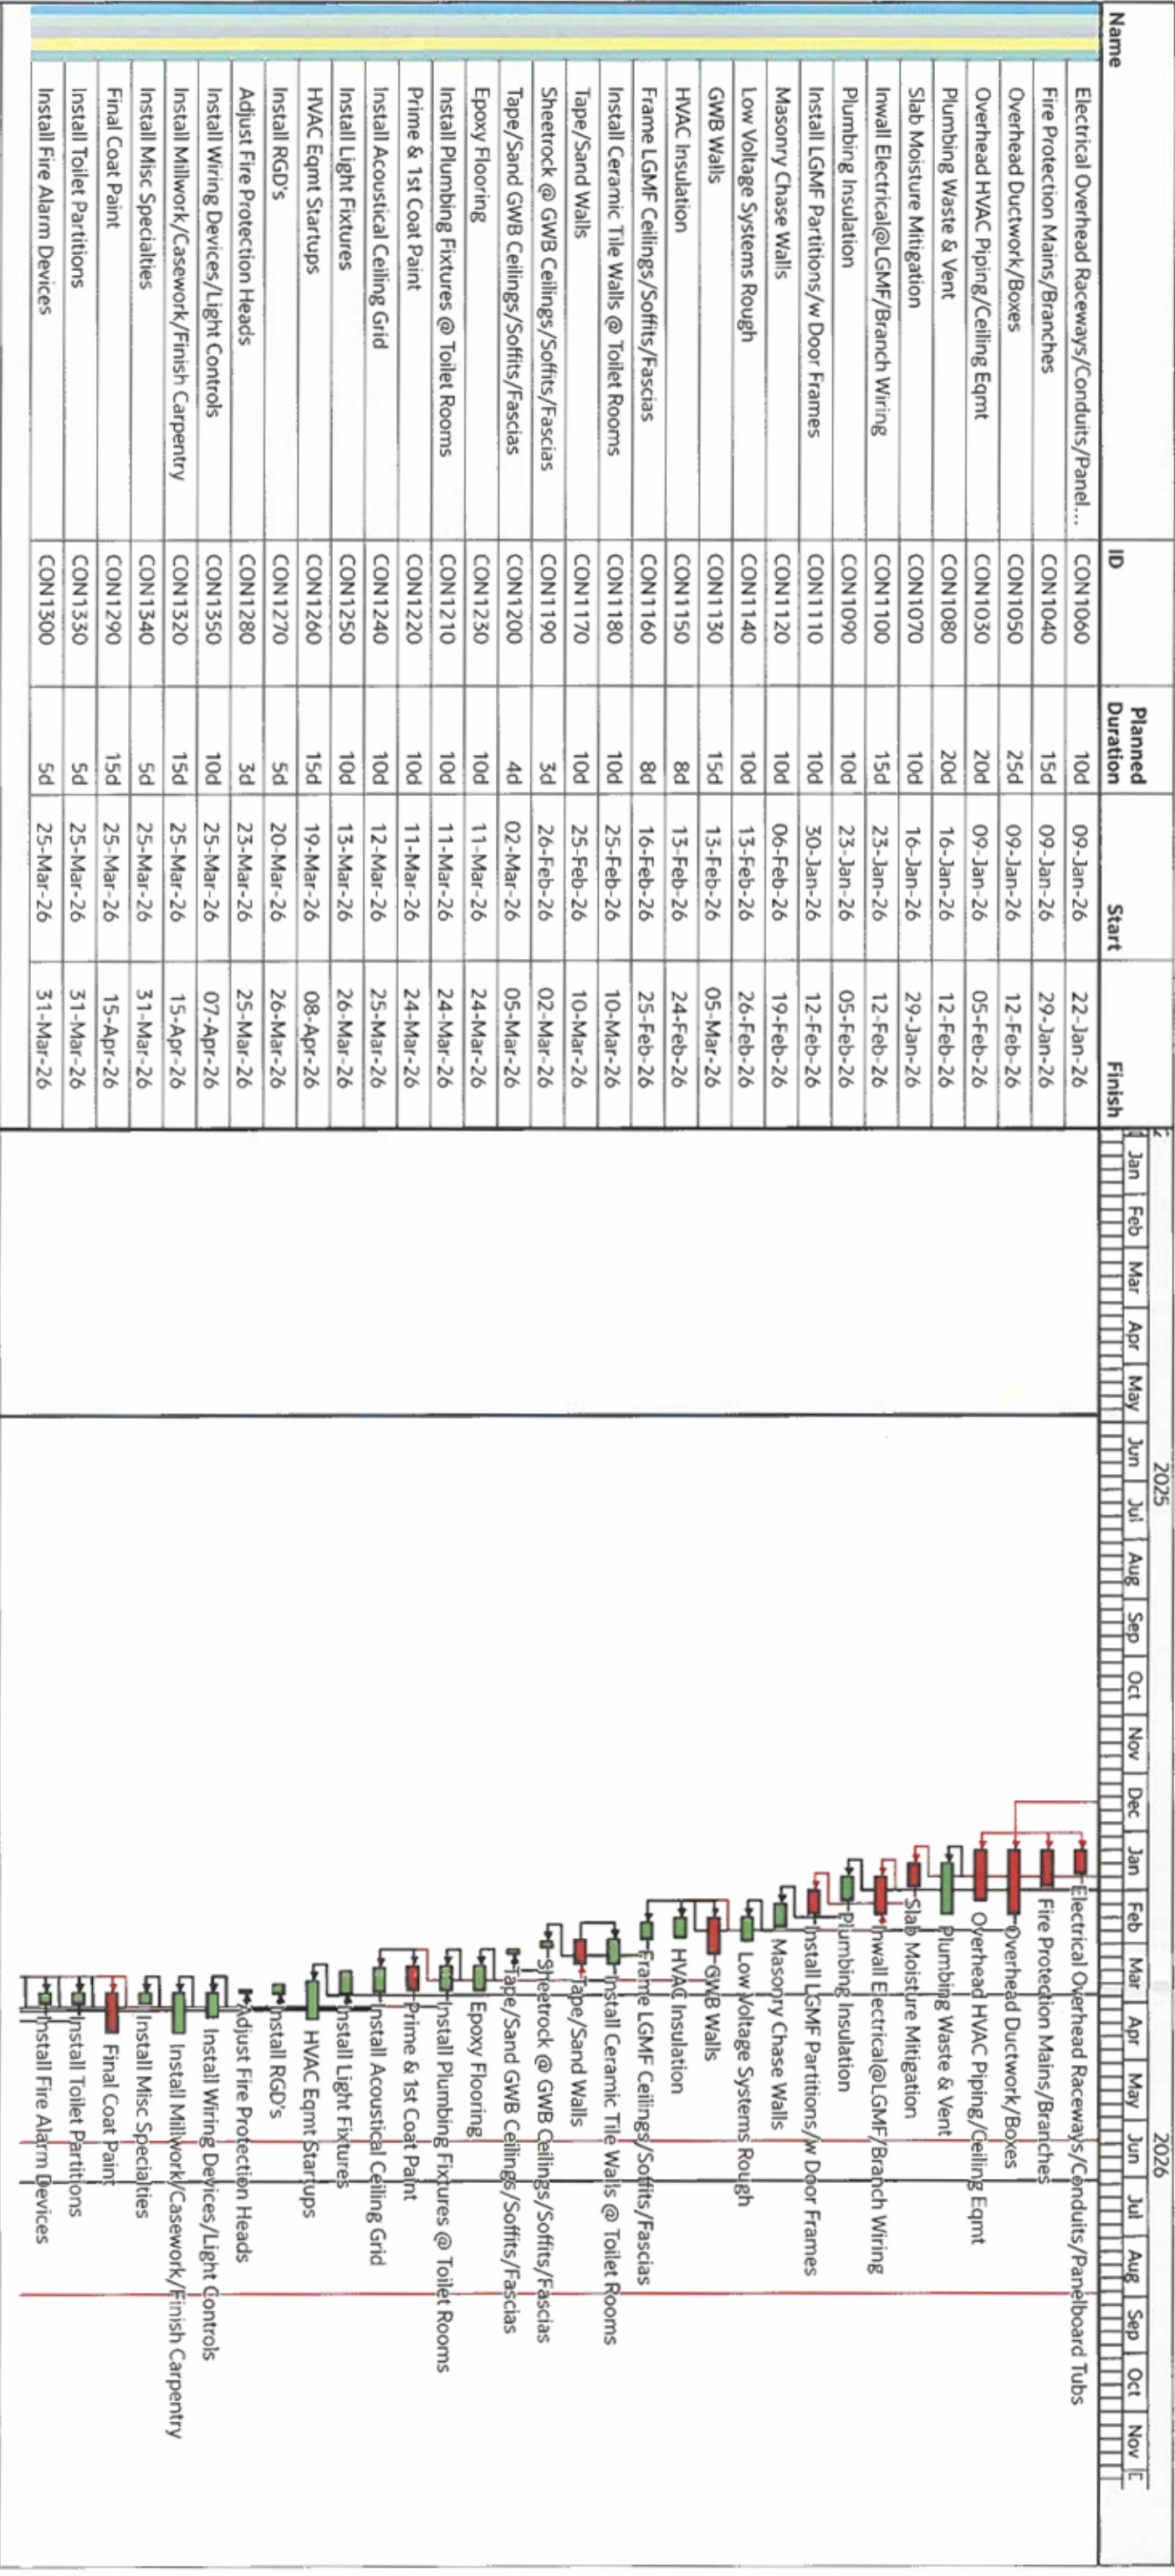

Oswegatchie Fire Station



- Current
- Progress
- Critical


Date	Revision	Checked	Approved
04-Mar-25	Update		
20-May-25	Update		
27-May-25	Update		

Waterford Connecticut



Project Schedule

Name	ID	Planned Duration	Start	Finish	2025												2026											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Hang Doors/Hardware	CON1360	15d	25-Mar-26	15-Apr-26																								
Install LV System Devices/Finishes (CCTV/Sec...	CON1310	5d	25-Mar-26	31-Mar-26																								
Final Above Ceiling Inspections	CON1370	2d	27-Mar-26	30-Mar-26																								
Padout Ceiling	CON1380	10d	31-Mar-26	14-Apr-26																								
Install Flooring/Base	CON1400	25d	01-Apr-26	06-May-26																								
Install Toilet Accessories	CON1410	3d	01-Apr-26	03-Apr-26																								
Fire Alarm Ringout	CON1390	10d	01-Apr-26	15-Apr-26																								
Testing, Balancing and Inspections	CON1420	10d	16-Apr-26	29-Apr-26																								
Pre-Punch/Broom Clean	CON1430	5d	07-May-26	13-May-26																								
Punchlist & Final Cleaning	CON1450	10d	14-May-26	28-May-26																								
Final Completion All Trades	CON1440	5d	14-May-26	20-May-26																								
Final Inspections & Substantial Completion	CON1460	5d	21-May-26	28-May-26																								
Owner Move-In / Occupancy	CON1470	15d	29-May-26	18-Jun-26																								
Site Improvements	SI	91d	21-Jan-26	28-May-26																								
Site Concrete	SITEI1000	15d	21-Jan-26	10-Feb-26																								
Stormwater Detention Systems	SITEI1010	10d	04-Feb-26	17-Feb-26																								
Paving	SITEI1020	10d	18-Feb-26	03-Mar-26																								
Site Improvements	SITEI1030	30d	08-Apr-26	20-May-26																								
Site Signage	SITEI1040	5d	21-May-26	28-May-26																								
Phase 2 Demolition of Existing Bldg.	WBS31	60d	29-May-26	21-Aug-26																								
Adjust temporary fence	DEMO1000	2d	29-May-26	01-Jun-26																								
Exist Bldg Hazmat Removal	DEMO1010	15d	02-Jun-26	22-Jun-26																								
Demolition of exist bldg.	DEMO1020	20d	23-Jun-26	21-Jul-26																								
Backfill existing foundations/grade site	DEMO1030	10d	22-Jul-26	04-Aug-26																								
Site Concrete	DEMO1040	5d	05-Aug-26	11-Aug-26																								
Paving	DEMO1050	5d	12-Aug-26	18-Aug-26																								
Site Improvements	DEMO1060	3d	19-Aug-26	21-Aug-26																								
Closeout	Close	40d	26-Jun-26	21-Aug-26																								
Final Completion (O&Ms/Asbuilts, etc...)	CLOS1000	40d	26-Jun-26	21-Aug-26																								

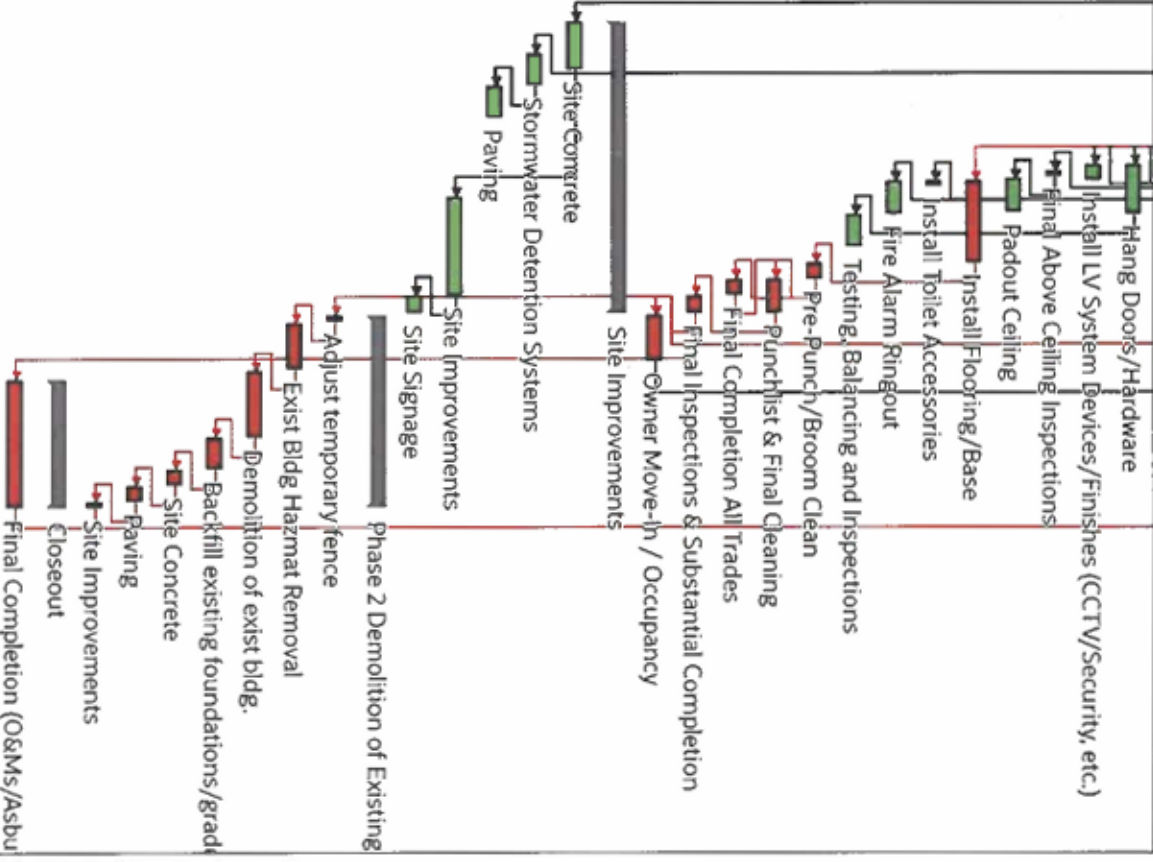

Oswegatchie Fire Station



DOWNES



Summary

- Current
- Progress
- Critical

Date Revision Checked Approved

04-Mar-25	Update		
20-May-25	Update		
27-May-25	Update		

Waterford Connecticut
